lients Name : Executive Engineer BBMP RR Nagara Divison, Bangalore

PROJECT PLANNING/SCHEDULE

roject Name : Improvements and Asphalting to Selected Cross Roads and Main Roads in Ward No.16 Jalahalli

Project Start Date : 18-Mar-22
Project End Date : 14-Sep-22
Project Length in Days : 180

Sl. No	Assignment	Unit	Boq Qnty	Start Date	End Date	No. of Working Days
1	KSRRB 300.46 Scarifying Bituminous course 50mm to 75mm thick along with premix carpet/ surface dressing by mechanical means attached with scarifier without disturbing the base and	Sqm	8610.30	19-Mar-22	21-Mar-22	2
2	KSRRB M300.14 Excavation for roadwork in all types of soil with hydraulic excavator of 0.9 cum bucket capacity including cutting and loading in tippers, trimming bottom and side slopes, in accordance with requirements of lines, grades and cross sections, and transporting to the	Cum	3874.64	22-Mar-22	25-Mar-22	3
3	Construction of granular sub-base Grading V as Sub base and drainage layer by providing coarse graded crushed stone aggregates of granite/ trap /basalt material, mixing in a mechanical mix plant at OMC, Carriage of mixed material to work	Cum	1722.06	26-Mar-22	30-Mar-22	4
4	KSRRB M400.17 Providing, laying, spreading and compacting crushed stone aggregates of granite / trap / basalt to wet mix macadam specifications including pre mixing the material with water at OMC in mechanical mix plant carriage of mixed method of tipper to site, laying in uniform layers with paver in sub-base/base course on well prepared surface and compacting with vibratory roller to achieve the desired density complete as	Cum	2152.58	1-Apr-22	4-Apr-22	3
5	KSRRB M500-6. Providing and applying primer coat with S.S. bitumen emulsion on prepared surface of granular base such as WMM ,including clearing of road surface and spraying primer at the rate of 0.60 kg / sqm using mechanical means complete as per Specifications. MORTH Specification No. 502 Complete with all lead and lift and as per the direction of the Engineer-in-Charge. Page No. 158/ Item No. 21.6/ PWD SR 2018-19 Issue Rate	Sqm	8610.30	5-Apr-22	5-Apr-22	1
6	KSRRB M500.17. Providing and laying dense graded bituminous macadam using crushed aggregates of specified grading, premixed with VG30 grade bituminous binder and, transporting the hot mix to work site, laying to the required grade, level and alignment, rolling with smooth wheeled, vibratory and tandem rollers to achieve the desired compaction as per MORTH table 500	Cum	430.52	5-Apr-22	6-Apr-22	1

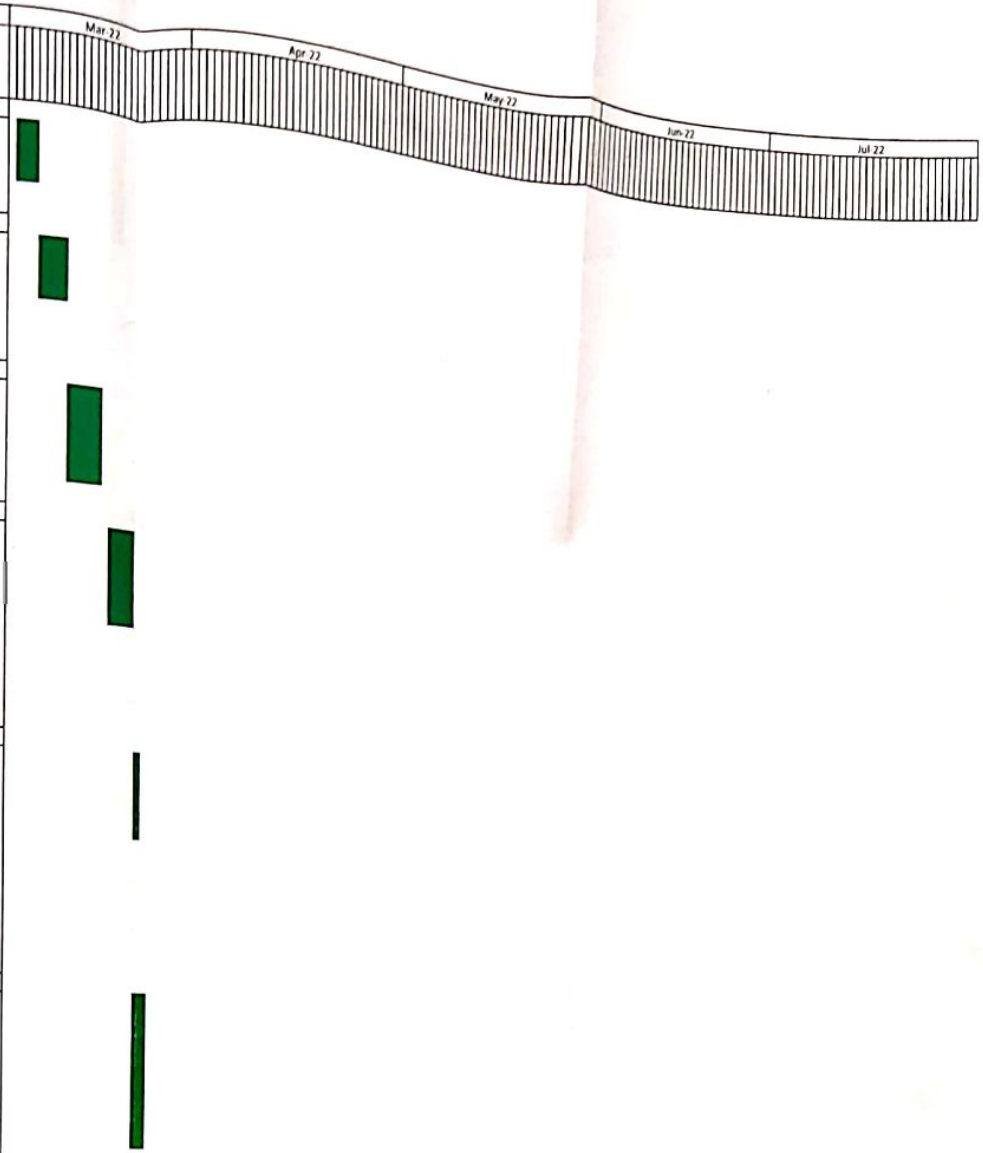

Scanned with CamScanner

Sl No	Assignment	Unit	Bag qty	Start Date	End Date	No of Working Days
1	[illegible]	Sqm	86[illegible]	7-Apr-22	7-Apr-22	1
8	[illegible]		344 41	7-Apr-22	8-Apr-22	1

Apr-22 | May-22 | Jun-22

CIVIL ONE ENGINEERS & CONSULTANTS

Scanned with CamScanner
